


ID	Task Name	Duration	Start	Finish	Predecessors	Jul 28, '02							Aug 4, '02							Au					
						T	W	T	F	S	S	M	T	W	T	F	S	S	M		T	W	T	F	S
1	Develop Web site prototype/template	20 days	Wed 7/24/02	Tue 8/20/02																					
2	Develop initial layout ideas	1 wk	Wed 7/24/02	Tue 7/30/02																					
3	Review and provide feedback	1 day	Wed 7/31/02	Wed 7/31/02	2																				
4	Complete prototype	1 wk	Fri 8/2/02	Thu 8/8/02	3																				
5	Review/provide feedback	3 days	Fri 8/9/02	Tue 8/13/02	4																				
6	Revise prototype	1 wk	Wed 8/14/02	Tue 8/20/02	5																				
7	Recruit newsletter staff	4 wks	Wed 7/24/02	Tue 8/20/02																					
8	Develop newsletter content	40 days	Wed 8/21/02	Tue 10/15/02	7																				
9	Writing	33 days	Wed 8/21/02	Fri 10/4/02																					
10	Research/write team leader profile	8 days	Wed 8/21/02	Fri 8/30/02																					
11	Research/write Strategic Planning in Action	2 wks	Mon 9/2/02	Fri 9/13/02																					
12	Research/write background articles	2 wks	Mon 9/16/02	Fri 9/27/02																					
13	Research/compile Strategic Planning calendar	2 wks	Mon 9/16/02	Fri 9/27/02																					
14	Write Letters to the Editor lead-in	2 days	Wed 9/18/02	Thu 9/19/02																					
15	Edit/revise articles	5 days	Mon 9/30/02	Fri 10/4/02	12,13,10,11																				
16	Photography	11 days	Mon 9/30/02	Mon 10/14/02																					
17	Submit photo list to photographer	1 day	Mon 9/30/02	Mon 9/30/02	10,11,12,13																				
18	Take photos	2 wks	Tue 10/1/02	Mon 10/14/02	17																				
19	Submit content to web designer	1 day	Tue 10/15/02	Tue 10/15/02	15,18																				
20	Content complete	0 days	Tue 10/15/02	Tue 10/15/02	19																				
21	Integrate content into web site	20 days	Wed 10/16/02	Tue 11/12/02																					
22	Import text and photos, layout articles	2 wks	Wed 10/16/02	Tue 10/29/02	20,6																				
23	Proof site	1 wk	Wed 10/30/02	Tue 11/5/02	22																				
24	Perform usability tests	1 wk	Wed 10/30/02	Tue 11/5/02	22																				
25	Revise site	1 wk	Wed 11/6/02	Tue 11/12/02	23,24																				
26	Issue 1 complete: site live	0 days	Tue 11/12/02	Tue 11/12/02	25																				
27	Promotion	33 days	Wed 10/9/02	Fri 11/22/02																					
28	Create flyer	2 wks	Wed 10/9/02	Tue 10/22/02	26FS-5 wks																				
29	Duplicate flyer 1	1 wk	Wed 10/23/02	Tue 10/29/02	28																				
30	Distribute flyer 1	3 days	Wed 10/30/02	Fri 11/1/02	29																				
31	Write/send kickoff email	3 days	Wed 11/13/02	Fri 11/15/02	26																				
32	Create flyer 2	1 wk	Wed 11/6/02	Tue 11/12/02	26FS-1 wk																				
33	Duplicate flyer 2	1 wk	Wed 11/13/02	Tue 11/19/02	32																				
34	Distribute flyer 2	3 days	Wed 11/20/02	Fri 11/22/02	33																				
35	Inservice session	1 day	Fri 11/1/02	Fri 11/1/02																					




Project: next newsletter
Date: Sat 8/23/03

Task Milestone External Tasks Deadline
 Split Summary External Milestone
 Progress Project Summary External Milestone

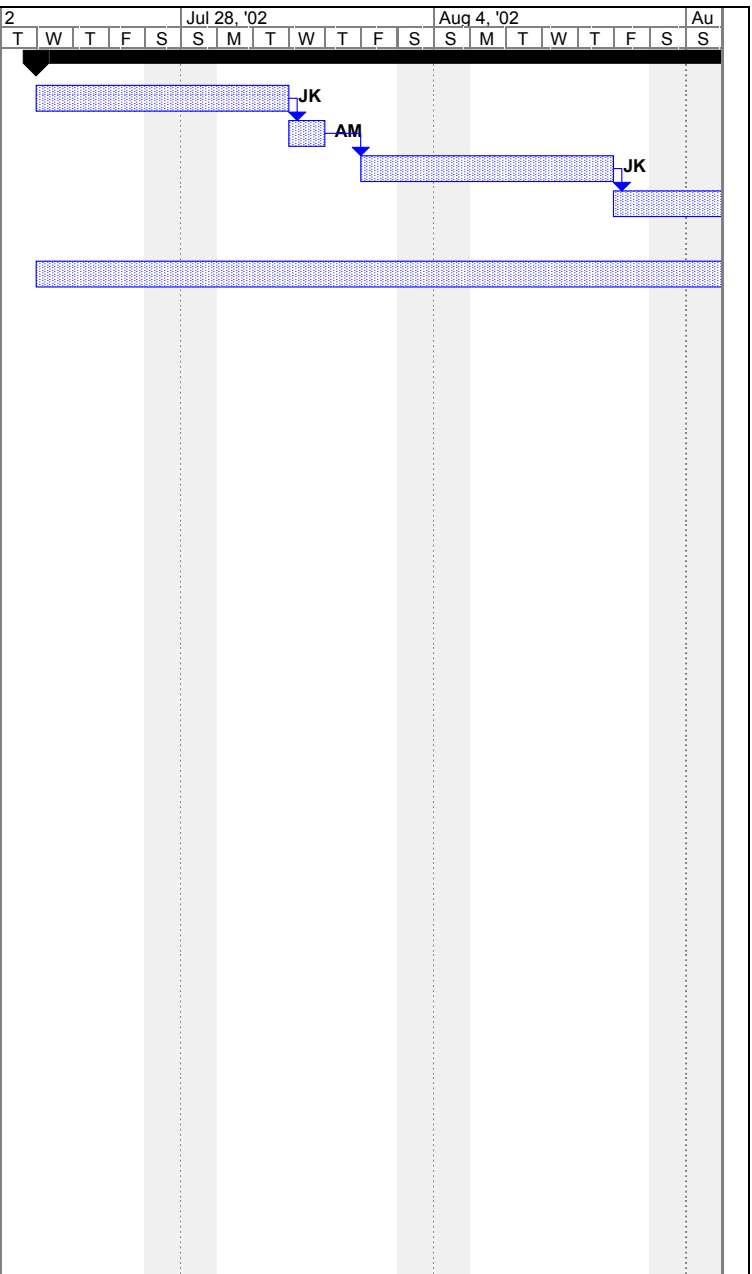

Project: next newsletter Date: Sat 8/23/03	Task		Milestone		External Tasks		Deadline	
	Split		Summary		External Milestone			
	Progress		Project Summary		External Milestone			

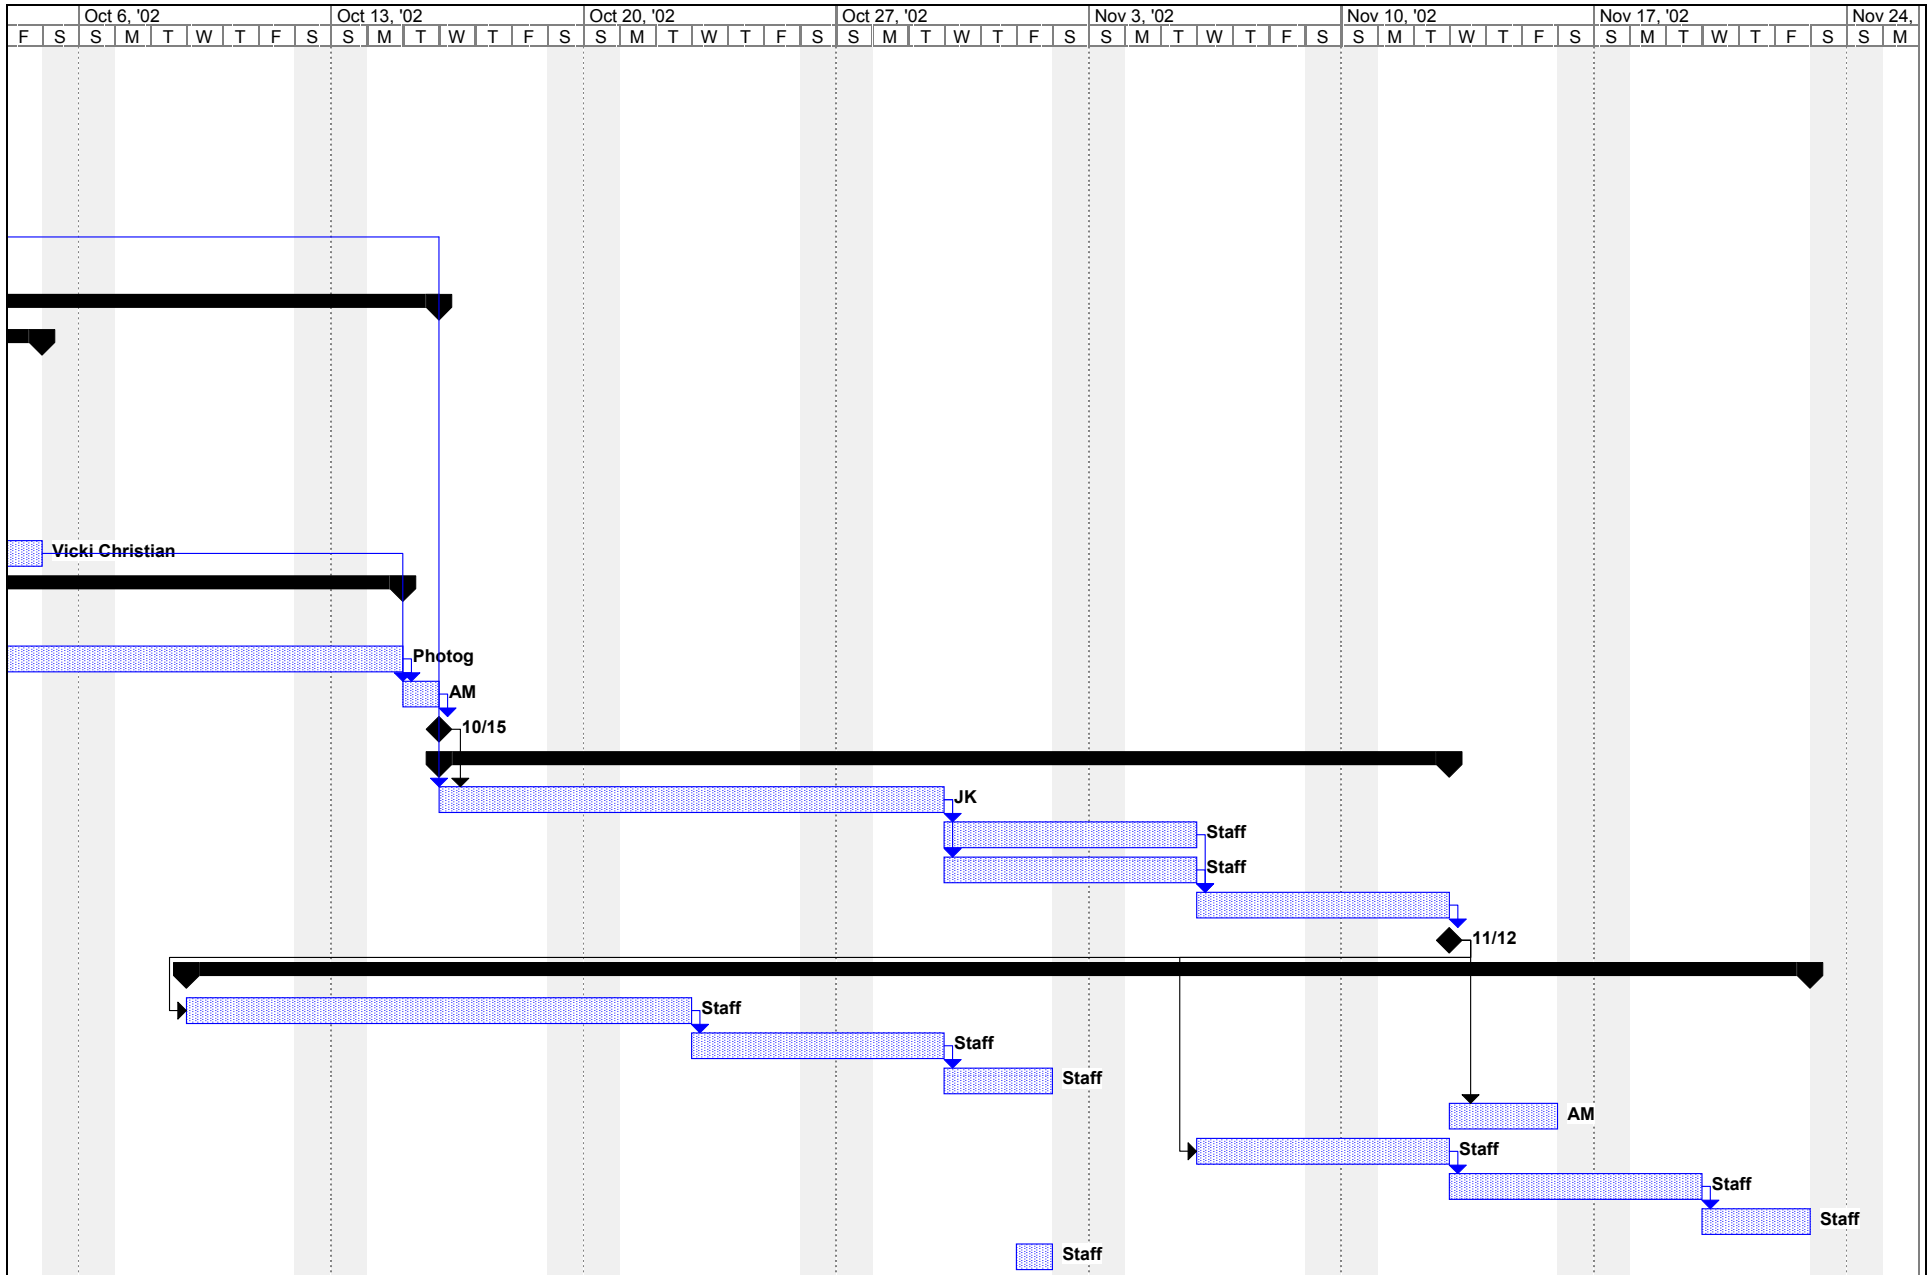

Project: next newsletter Date: Sat 8/23/03	Task		Milestone		External Tasks		Deadline
	Split		Summary		External Milestone		
	Progress		Project Summary		External Milestone		
